

Applied Agility

Setting Up an Agile Practice

Barry Hawkins
barry@alltc.com
@barryhawkins



Scrum

sprint planning

cross-functional participation

account for all required
hours

	A	B	C	D	E	F	G	H	I	J	K	L	M	N
1	Person	Hours		Development Tasks	Hours		QA Tasks	Hours		Data Tasks	Hours		Product Tasks	Hours
2	Frodo	35		Fix Print This Listing	2		Fix Print This Listing	1		Lead record My Favorite Sessio	1		Fix Print This Listing	1
3	Sam	40			4			2			2		Verizon lander page	1
4	Merry	30			2		Key Accts. Robots.txt changes	1			1		Google Maps display blank	1
5	Pippin	40			2		Lead record My Favorite Sessio	4			2		Property thumbnails MIA	1
6	Legolas	0		Key Accts. Robots.txt changes	2			2		Modify Uncle Bob hyperlink	1		Internal server errors	1
7	Gimli	40		Lead record My Favorite Sessio	2		Modify hyperlink	1		Metro SR Check Ava. Lead Sub	1		Metro SR	1
8	Development Total	185			2		Verizon lander page	2						
9					4		Google Maps display blank	2						
10	Boromir	0		Verizon lander page	2		Property thumbnails MIA	2						
11		0			2		Internal server errors	1						
12				Google Maps display blank	2		Metro SR Check Ava. Lead Sub	2						
13	QA Total	0			4		Metro SR	1						
14				Property thumbnails MIA	2		No Back Button in Firefox	2						
15					2									
16	Aragorn	0		Internal server errors	2									
17					4									
18	Data Total	0		Metro SR Check Ava. Lead Sub	6									
19				Metro SR	2									
20				XYZ Spike	80									
21	Gandalf	0								TOTAL	8		TOTAL	6
22														
23	NetOps Total	0								NetOps Tasks	Hours			
24	Overall Total	185								Internal server errors	1			
25														
26	Total Hours:	168												
27	Dev Hours Left:	57												
28	QA Hours Left:	-23												
29	Data Hours Left:	-8												
30	NetOps Hours Left:	-1												
31	Product Hours Left:	-6												
32														
33														
34														
35														
36														
37														
38														
39														
40														
41														
42														
43				TOTAL	128		TOTAL	23		TOTAL	1			

43				TOTAL	128		TOTAL	23		TOTAL	1			
44														
45														
46														
47														
48														
49														
50														
51														
52														

Person	Hours	Flash Tasks	Hours	Java Tasks	Hours
John Doe	42	EUP 0.24 Protogen Migration	1	EUP 0.24 Protogen Migration	2
Jane Doe	42		1		2
Jennifer Doe	42		1		2
Jebediah Doe	42		1		2
Flash Total	168		1		2
			1		2
Jerry Doe	37		1		2
Dolores O'Riordan	32		1		3
		Shared Spaces First Pass	2		5
Java Total	69		5		10
Overall Total	237		10		5
			5		3
Total Hours:	189		10		3
Flash Hours Left:	42		10		2
Java Hours Left:	6	Shared Spaces Item Place	3		3
			2		5
			10		5
			5		5
			2		2
			10		2
			5		2
Java Hours Left:	6	Shared Spaces Item Place	3		3
Flash Hours Left:	42		10		5

task board

To DO

SQL - Can we load
scripts to drop files
into Endowment
QA? -QA

Create VM for
LAB TRACK & LOG 10

SET UP SRS -
VERSION 2 AND
BUILD SO THAT
FUTURE ERRORS
FOR CONT. BLDG.
DEV 2 HRS
SD 2 HRS

PREPARE
C.A.F.
DEV 1 HR
SD 2 HR

Allow Add'l Member of
household to be enrolled
via Bulk Enrollment, so it
eliminates Partner Ops
need to remediate/
add manually, so there is
increased throughput of new enrollees

QA

QA

ID ADD'L
MEMBER BY
COMPARING
DATA 8 hrs.

CALL WS
TO ADD
ADD'L
MEMBER 4 hrs.

ID ADD'L
MEMBER
FAILURE
MESSAGE 1 hr.

UPDATE
REPORTING
SCRIPT FOR
FAILED
ENROLLMENTS 4 hrs.

Review Reports
by DBA 2 HR

DEV/DBA
SCRIPT
FEEDBACK
RESOLUTIONS 2 hrs.

As ODS, I can appropriately
structure Bulk Enrollment
data relationships so that
enhancements are
scalable/flexible.

DESIGN SESSION 2

CREATE NEW TABLES
- VERIFY
- ERUITE 2

PREPARE DATA
MIGRATION PLAN 2

PERFORM DATA
MIGRATION 1

CREATE TRIGGER
SCRIPTS 1

ANALYZE CURRENT
BULK DB TABLES 1

DEV DB DESIGN
SESSION 2

PREPARE DATA
MIGRATION PLAN
W/ DBA & USING
CURRENT DB
DESIGN & NEW
DB TABLES 2 hrs.

CREATE
TABLE
SCRIPTS 2 hrs.

CREATE SEQUENCE
SCRIPTS 1

CHANGE, UPDATE,
CREATE ENTRY
SCRIPTS 12

CHG. BIZ
LOGIC TO
INCORPORATE
UPDATED
ENTRY BONUS 4 hrs.

QA
?

Bulk enroll all valid
members within a valid
account (household),
so Partner Operations
reduce enrollment remediation.

UPDATE BULK
VALIDATION
MECHANISM 8

REPORTING
UPDATES
TO SHOW
FAILED MEMB
& SHOW SUCCESS
REMEDATION 2 hrs.

Order of
Validation 2A 3 HR

UPDATE ERROR
LOGS 2A 2

UPDATE
PARTNER
IMP GUIDE 2A 3 HR

QA

QA

BULK ENROLL
BULK ENTRY

CPES VMLab
Mgt Track & Log
10

TO DO:

As a ^{non-piping} member, I
only see a CC upgrade
path if I have a basic
plan so it's clear
what my upgrade
path is.

Analyze existing code	Regression test for pay + non-pay patterns codes.	Promote code to DEV-INT.	Document code changes.	IT Biz vs SCEA for items in regarding to the upgrade
4hr	4hr	1hr	1hr	

D.C. + Test Case Doc 1hr.	QA Script update MemID NonMemID Comp/Non Comp 2	Activate bus rules for reporting 1	QA-QA Test 4	DEV-QA Test AP WS MPL 4
---------------------------------------	---	--	-----------------	-------------------------------------

Via SF -
determine
method for
identifying
parameters not
eligible for upgrade
1hr

Expanding on
outcome of
determine if
data is already
in reporting DB
through
1hr


As a myll user,
I can see the data in
the T&C, so the
I know my agreement
with CC.

QA Script & Test 2	Obtain T&C update date. 1	Update T&C table field, require test document & promote to dev-int. 1
--------------------------	---------------------------------	---

As a member that has
never enrolled in CC,
I get 1 baseline report
so I clearly know my
reporting table status.

As a member that has
never enrolled in CC,
I get an alert notification
as soon as one is available
to view in my CC.


TO DO	TEST	WIP	Dev-Int	DONE
[Sticky Note]		[Sticky Note]		[Sticky Note]
[Sticky Note]		[Sticky Note]		[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]				[Sticky Note]
[Sticky Note]		[Sticky Note]	[Sticky Note]	[Sticky Note]

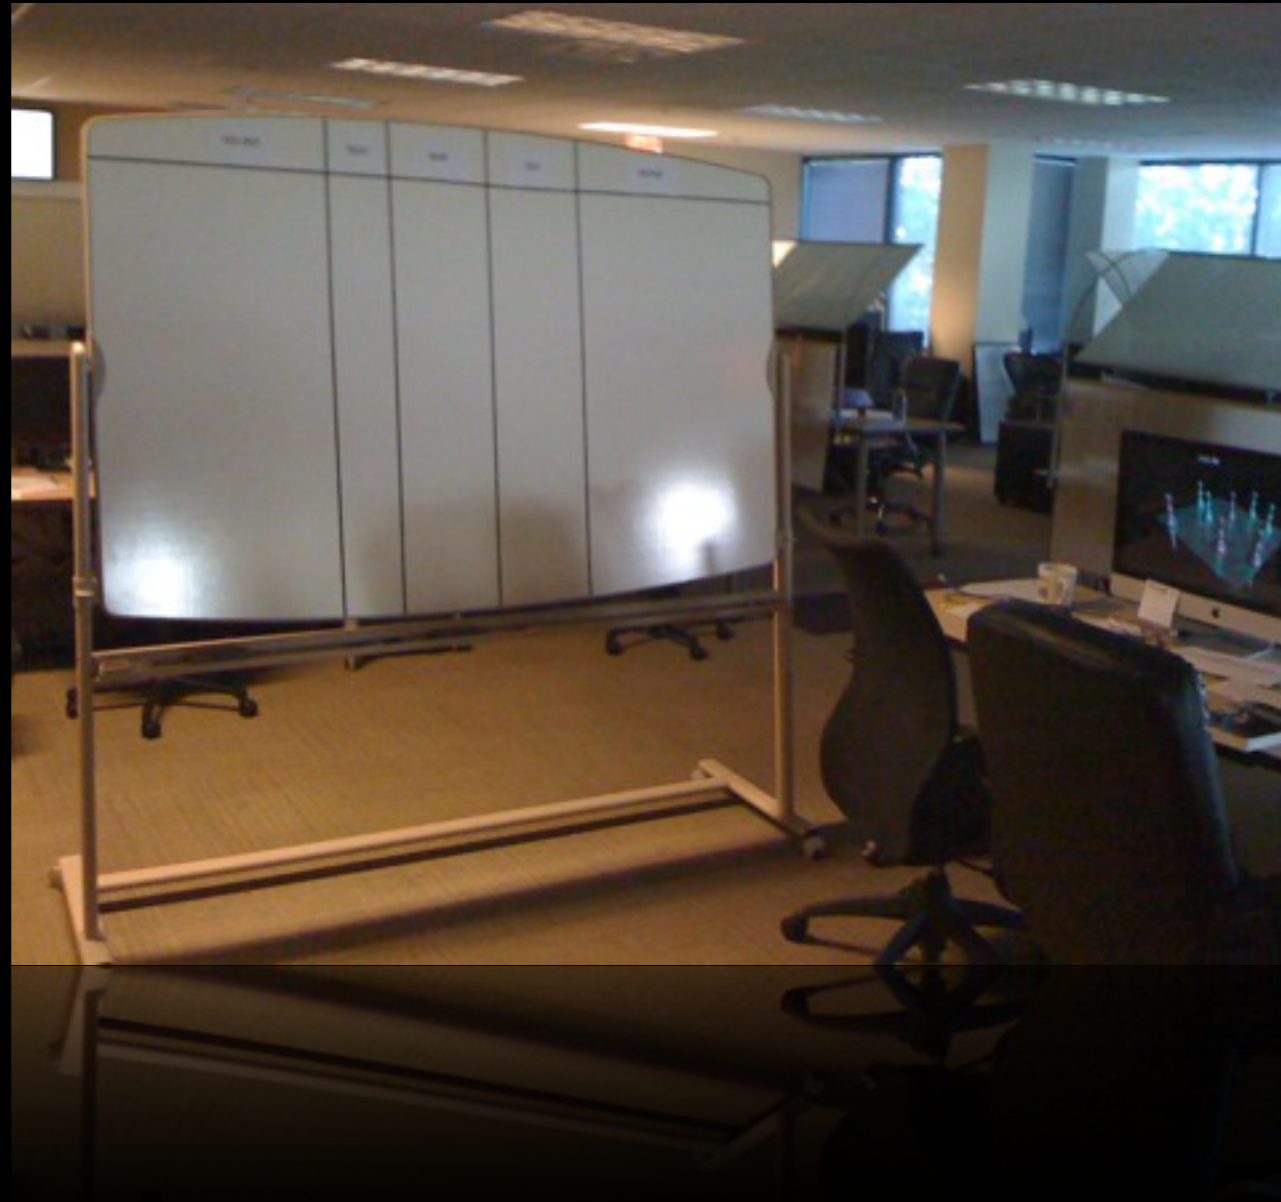

TO DO	TEST	WIP	QA	DONE

RED TEAM

TO DO	TEST	WIP	ACCEPT	DONE
<p>Task 1: [Handwritten notes]</p>			<p>[Green sticky]</p>	
<p>Task 2: [Handwritten notes]</p>			<p>[Red sticky]</p>	
<p>Task 3: [Handwritten notes]</p>				<p>[Yellow sticky]</p>
<p>Task 4: [Handwritten notes]</p>		<p>[Red sticky]</p>		<p>[Yellow sticky]</p>
<p>Task 5: [Handwritten notes]</p>			<p>[Yellow sticky]</p>	<p>[Green sticky]</p>
<p>Task 6: [Handwritten notes]</p>			<p>[Yellow sticky]</p>	<p>[Orange sticky]</p>
<p>Task 7: [Handwritten notes]</p>		<p>[Yellow sticky]</p>		
<p>Task 8: [Handwritten notes]</p>				
<p>Task 9: [Handwritten notes]</p>				
<p>Task 10: [Handwritten notes]</p>				
<p>Task 11: [Handwritten notes]</p>				
<p>Task 12: [Handwritten notes]</p>				
<p>Task 13: [Handwritten notes]</p>				
<p>Task 14: [Handwritten notes]</p>				
<p>Task 15: [Handwritten notes]</p>				

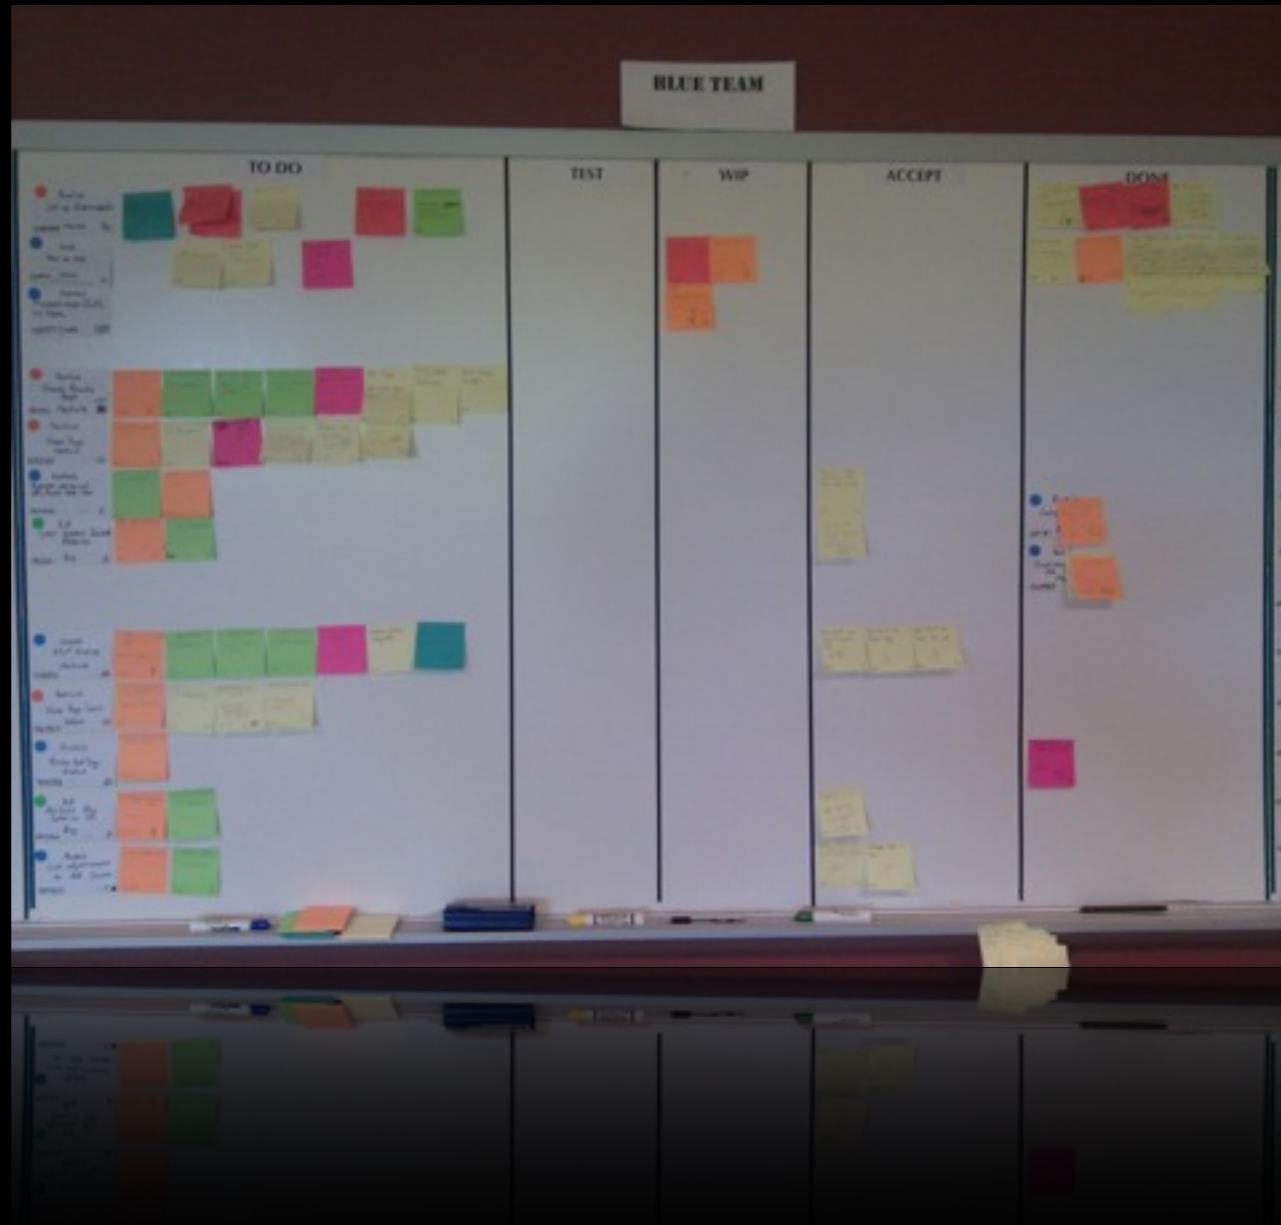



burndown chart

	A	B	C	D	E	F	G	H	I	J	K	
1	Story	Hours	Day 1	Day 2	Day 3	Day 4	Day 5	Day 6	Day 7	Day 8	Day 9	
2	Google Maps display blank (20)	9	3	1	0	0	0	0	0	0	0	
3	Property thumbnails MIA (13)	7	3	1	0	0	0	0	0	0	0	
4	Internal server errors (13)	9	3	3	3	0	0	0	0	0	0	
5	Metro SR Check Ava. Lead Sub. Key/val (13)	9	4	4	0	0	0	0	0	0	0	
6	Metro SR Rent Specials link shows js error (8)	4	2	2	0	0	0	0	0	0	0	
7	Modify ██████████ hyperlink (13)	2	3	3	0	0	0	0	0	0	0	
8	Key Accts. Robots.txt changes (5)	3	4	4	4	0	0	0	0	0	0	
9	QA Bulk Story for ██████████ (40)	2	16	12	20	0	0	0	0	0	0	
10	No Back Button in Firefox (5)	2	2	2	2	0	4	4	4	2	2	
11	██████████ Spike (100)	80	70	44	42	42	38	32	28	28	18	
12	Verizon lander page (13)	7	7	7	4	4	4	4	3	1	0	
13	Lead record ██████████ Session ID (40)	20	20	20	20	20	20	20	12	6	2	
14	██████████ Fix Print This Listing (20)	14	14	14	14	14	14	14	14	3	0	
15	Relo Form text (20)		7	1	31	31	31	31	31	16	1	
16	██████████ - Unable to save listing via Detail Page		?	2	2	2	6	6	-	-	-	
17	AG - Detail Page needs text update for the School "note" information		?	?	?	2	5	5	3	3	1	
18	IE6 pagination bar "Page 1 of 68" only partially showing		?	?	?	?	3	3	3	2	2	
19	WebTrends - Create multitrack tag wt_ag_0010 for Property Details Google Map "Click for Map" image		?	?	?	2	4	4	2	2	1	
20	Migrate to new git workflow (20)			?	?	2	0	0	0	0	0	
21	Apply wt_ag_001s to get Driving Dir. Submit via press Enter (5)							3	0	0	1	
22	Remove wt_ag_001s from Find A Mover (3)							5	3	3	1	
23	WebTrends leadcount value is incorrect for all Personalization lead submits (13)							3	1		1	
24	██████████ does not render top right of Builder Search (?)								3	1	0	
25	██████████ Unable to remove last refinement on search results (13)									6	0	
26		Total	168	158	120	142	119	129	134	107	73	30

burndown tracking

workspace



story writing sessions

backlog grooming

sprint log

sprint review

sprint retrospective

software releases

wow, that's simple

almost noone does it



all things computed

Barry Hawkins
barry@alltc.com
@barryhawkins
